

D	0	Task Name			Work	Duration	Start	
0	Open Rosters		450 hrs	37.13 days	Tue 11/25/14			
1		Analyze & Plan			40 hrs	4.75 days	Tue 11/25/14	
2	~	 Detailed Review of Documents (Prototype, Wireframe & Unique Pages Designs) and Gap Analysis 		• •	, 16 hrs	2 days	Tue 11/25/14	
3	~	Create High Level Project Schedule based on initial document review		based on initial	2 hrs	0.25 days	Thu 11/27/14	
4	~	Internal Discussion (Functional and Technical Feasibility)		Technical	10 hrs	0.63 days	Thu 11/27/14	
5		Document Ope	en Issues & share wit	h Client	2 hrs	0.13 days	Thu 11/27/14	
6		Response / Dis	scussion		8 hrs	0.5 days	Mon 12/1/14	
7		Revise Project	Plan		2 hrs	0.25 days	Mon 12/1/14	
8		Development En	vironment Setup		2 hrs	0.25 days	Fri 11/28/14	
9		Configure Repository & provide team access, Set up Development environment		m access, Set up	2 hrs	0.25 days	Fri 11/28/14	
10		Architecture			64 hrs	7 days	Mon 12/1/14	
11		Database Desig	n		24 hrs	3 days	Mon 12/1/14	
12		Codebase Fram	ework		12 hrs	2 days	Thu 12/4/14	
13		Code Architectu	ıre		12 hrs	2 days	Mon 12/8/14	
14		Review with Sushan & Updates			16 hrs	4 days	Thu 12/4/14	
15		Development			192 hrs	14.5 days	Tue 12/9/14	
16		Project briefin	g & document reviev	I	4 hrs	0.5 days	Tue 12/9/14	
Task				nactive Task		Start-only	С	
Project: Open Rosters Date: Wed 12/3/14			Split		nactive Milestone	\Diamond	Finish-only	_
			Milestone	•	nactive Summary	\bigcirc	Deadline	$\hat{\Phi}$
			Summary		Manual Task		Critical	
		12/3/14	Project Summary		Duration-only		Critical Split	
			External Tasks		Manual Summary Rollup		Progress	
Ext			External Milestone	♦	Manual Summary			
					Page 1			


D	0	Task Name			Work	Duration	Start	
17	Ů	Frontend Dev	elopment		84 hrs	14 days	Tue 12/9/14	
18		Login Page		4 hrs	0.5 days	Tue 12/9/14		
19		Dashboard			4 hrs	0.5 days	Wed 12/10/14	
20		Import Mod	ule / Import Rosters		24 hrs	3 days	Wed 12/10/14	
21		API Develop	ment		24 hrs	3 days	Mon 12/15/14	
22		View Data S	election		16 hrs	2 days	Thu 12/18/14	
23		Help Section	1		4 hrs	0.5 days	Mon 12/22/14	
24		Peer Code R	leview		8 hrs	1 day	Fri 12/26/14	
25		Application Do	evelopment		104 hrs	13 days	Wed 12/10/14	
26		Developer M	anagement		16 hrs	2 days	Wed 12/10/14	
27		Import Modu	ıle / Import Rosters		24 hrs	3 days	Fri 12/12/14	
28		API Development		24 hrs	3 days	Wed 12/17/14		
29		View Data Selection		16 hrs	2 days	Mon 12/22/14		
30		Developmen	t of Installer wizard		16 hrs	2 days	Wed 12/24/14	
31		Peer Code R	leview		8 hrs	1 day	Fri 12/26/14	
32		QA			52 hrs	25 days	Mon 12/1/14	
33		Test Case Crea	ntion		8 hrs	1 day	Mon 12/1/14	
34		Test Case Revi	ew & Finalization		8 hrs	1 day	Tue 12/2/14	
35		Prepare & Sen	d Release Note to QA	A for Round 1	2 hrs	0.25 days	Mon 12/29/14	
36		Testing Round 1		12 hrs	1.5 days	Tue 12/30/14		
37		Bug Fixing & Release for Review			12 hrs	0.75 days	Wed 12/31/14	
			Task		Inactive Task		Start-only	
Project: Open Rosters Date: Wed 12/3/14			Split		Inactive Milestone	♦	Finish-only	
			Milestone	♦	Inactive Summary	$\overline{\hspace{1cm}}$	Deadline	$\hat{\mathbf{T}}$
			Summary		Manual Task		Critical	
		12/3/14	Project Summary		Duration-only		Critical Split	
			External Tasks		Manual Summary Rollup		Progress	
			External Milestone	♦	Manual Summary			

Page 2

ID		Task Name	Work	Duration	Start
	0				
38		Testing Round 2	6 hrs	0.75 days	Thu 1/1/15
39		QA Sign Off	2 hrs	0.25 days	Fri 1/2/15
40		Demo to Client	2 hrs	0.5 days	Mon 1/5/15
41		UAT	96 hrs	6 days	Mon 1/5/15
42		Testing	32 hrs	4 days	Mon 1/5/15
43		Bug Fixing, Internal Review & Release for Review	48 hrs	2 days	Wed 1/7/15
44		Final Review before Go Live	16 hrs	2 days	Fri 1/9/15
45		GO Live	2 hrs	0.25 days	Tue 1/13/15
46		Project Closure Meeting and Sign Off	2 hrs	0.13 days	Thu 1/15/15



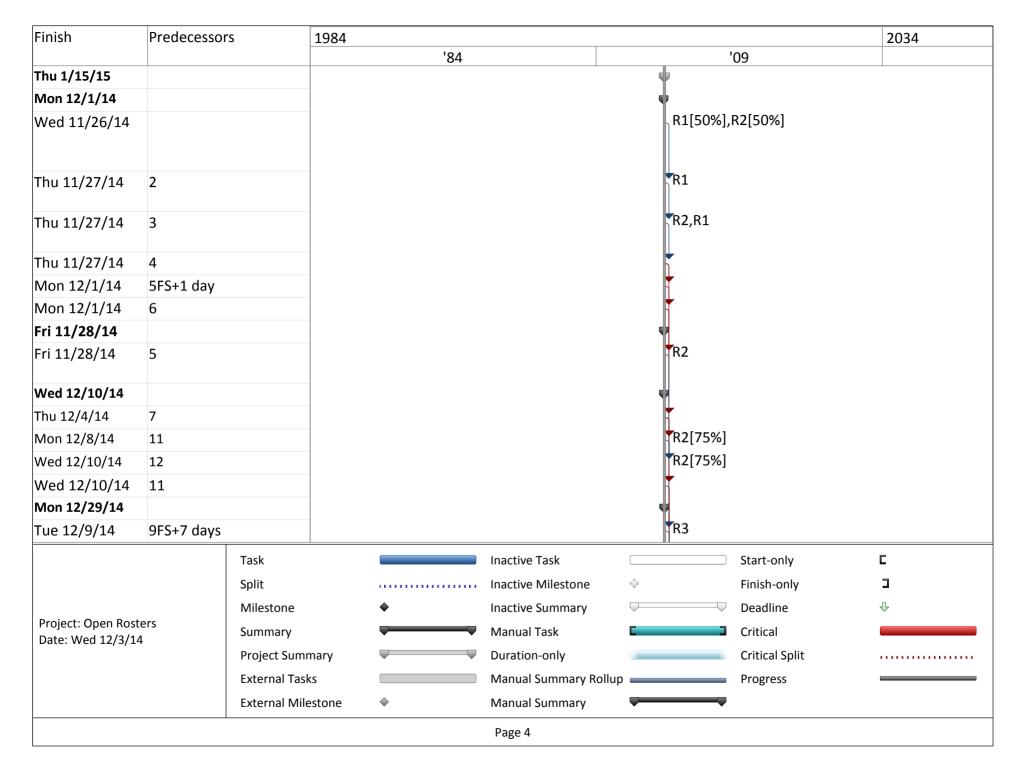

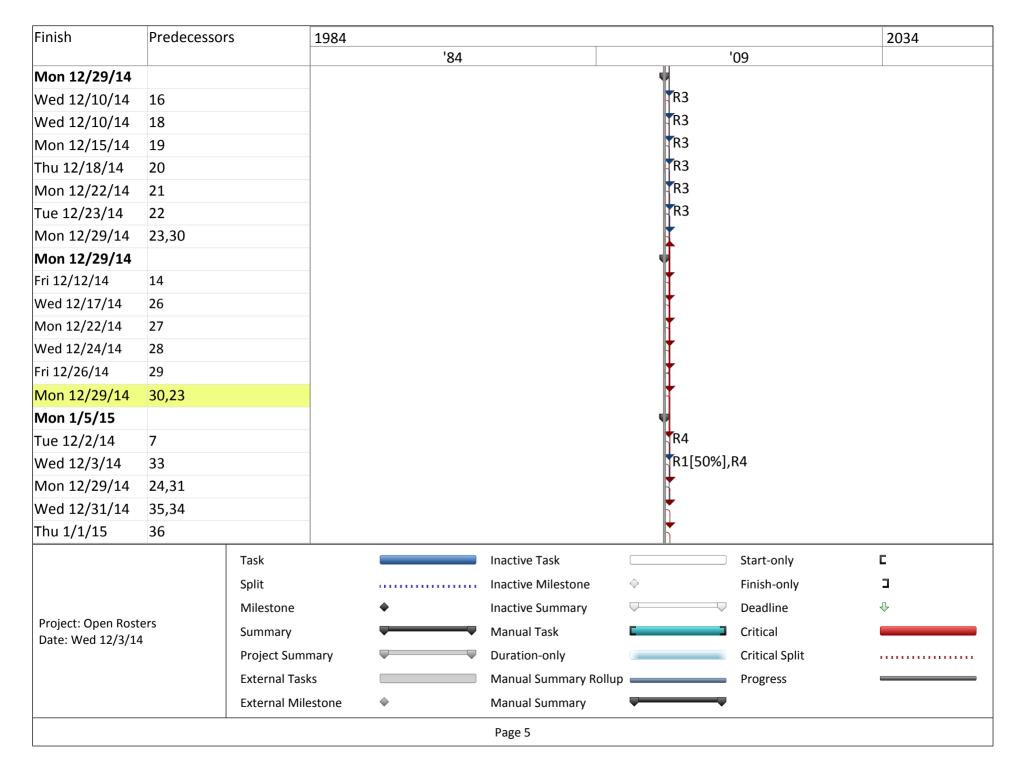

Finish	Predecessors	1984		
		'84	'09	
Thu 1/1/15	37		<u> </u>	
Fri 1/2/15	38		<u> </u>	
Mon 1/5/15	39FS+1 day		†	
Tue 1/13/15			•	
Fri 1/9/15	40		\rightarrow	
Fri 1/9/15	42FS-2 days		 	
Tue 1/13/15	43		\	
Tue 1/13/15	44		K	
Thu 1/15/15	45FS+1 day		 	

